



# Engineering Services Manager's Report

Engineering and Operations Committee

Item 7b

January 10, 2022

# Construction and Procurement Contracts


## November 2021

Construction & Procurement Contracts Through November 2021	
Number of Contracts at end of November 2021	39
Total Bid Amount of Contracts in Progress at end of November 2021	\$272M
Contracts Awarded in November 2021	3
Contracts With Notice To Proceed Issued in November 2021	0
Contracts Completed in November 2021	0
Contract Gross Earnings in November 2021	\$3.9M

# CRA – Gene Wash Reservoir Discharge Valve Replacement



Removing the Old Valve

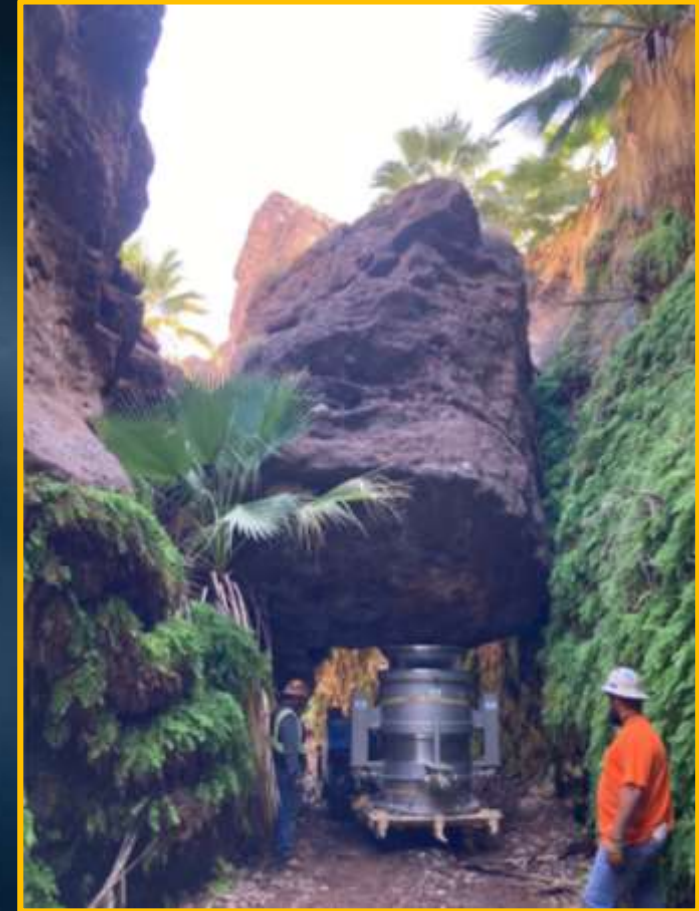

Transporting the Fixed Cone Valve



# CRA – Gene Wash Reservoir Discharge Valve Replacement



Fixed Cone Valve Installation Complete

# CRA Mile 12 Flow Monitoring Station Upgrades Project

- Completed Tasks:
  - Installation of the new CMU wall extension.
- On-Going Tasks:
  - Excavation for the electrical grounding circuit and rods.
  - Installation of the electrical grounding grid.
- Contract Amount:
  - \$2,022,000 / Paid to Date: 4.5%
- Original Contract Duration:
  - 220 Working Days / 45.5% to date

# CRA Mile 12 Flow Monitoring Station Upgrades Project





# Headquarters Security Contract



The Security Desk Area (Inside the Dust Containment) under Construction

